EARNED VALUE GIÁ TRỊ THU ĐƯỢC


Earned value management helps you quantify the performance of a project. It compares costs and schedules to a baseline to determine if the project is on track.

If the charts don't look right, make sure you have set a baseline, assigned costs to tasks or resources, and entered progress.

Quản lý giá trị thu được giúp bạn định lượng hiệu suất của một dự án. Nó so sánh chi phí và lịch trình với đường cơ sở để xác định xem dự án có đi đúng hướng hay không.

Nếu biểu đồ trông không ổn, hãy đảm bảo bạn đã đặt đường cơ sở, phân bổ chi phí cho nhiệm vụ hoặc tài nguyên và nhập tiến độ.




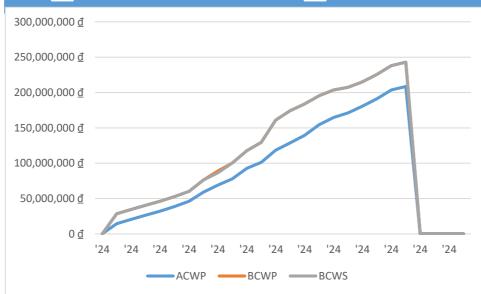

EARNED VALUE OVER TIME


The project's earned value based on the status date. If actual cost (ACWP) is higher than earned value (BCWP), then the project is over budget. If planned value (BCWS) is higher than earned value, then the project is behind schedule.

Learn more about earned value

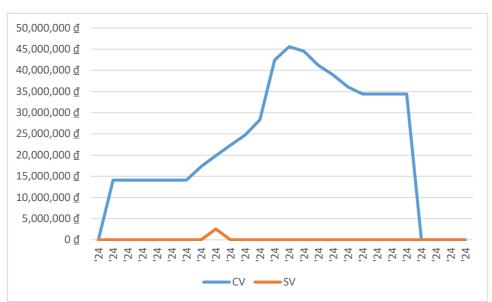

VARIANCE OVER TIME

Cost and schedule variances for the project based on status date. If CV is negative then, the project is over budget. If SV is positive then the project is behind schedule.

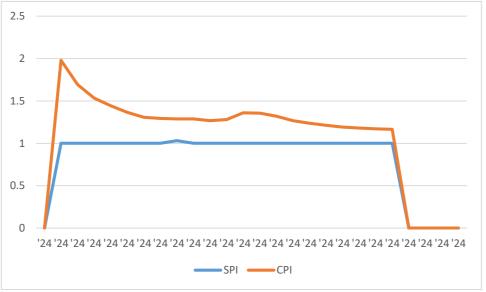

INDICES OVER TIME

Cost and schedule performance indices for the project based on status date. The greater the performance index, the more on schedule and cost saving the project.
